



**ROADWAY PROJECT UPDATES
DECEMBER 2025
OFFICE OF THE COUNTY ENGINEER**

SW 49TH/40TH AVE PHASE 1

NEW 4-LANE ROAD FROM SW 66TH ST TO SW 43RD ST RD


- Completed half of the roadway in front of the Heath Brook entrance.
- 3 of 4 DRAs constructed.
- Signal at SW 43rd St Rd in flash. Awaiting City approval to fully activate signal.
- Evaluating lane closure/detour options for construction at SW 66th St.
- Westbound Turn Lane at SW 43rd St Rd and SW 40th Ave.
- Eastbound and Westbound Turn lanes at SW 42nd St and SW 27th Ave.



NW/NE 35TH ST PHASE 1B


ADD 2 LANES FROM 600 FT E OF W ANTHONY RD TO NE JACKSONVILLE RD

- Acquired right-of-way from 18 of 47 parcels. Working on acquisition for remaining 29 parcels.
- Design completion estimated in June 2026.
- Beginning permit update with Water Management District. Minimum 4-month permitting process.

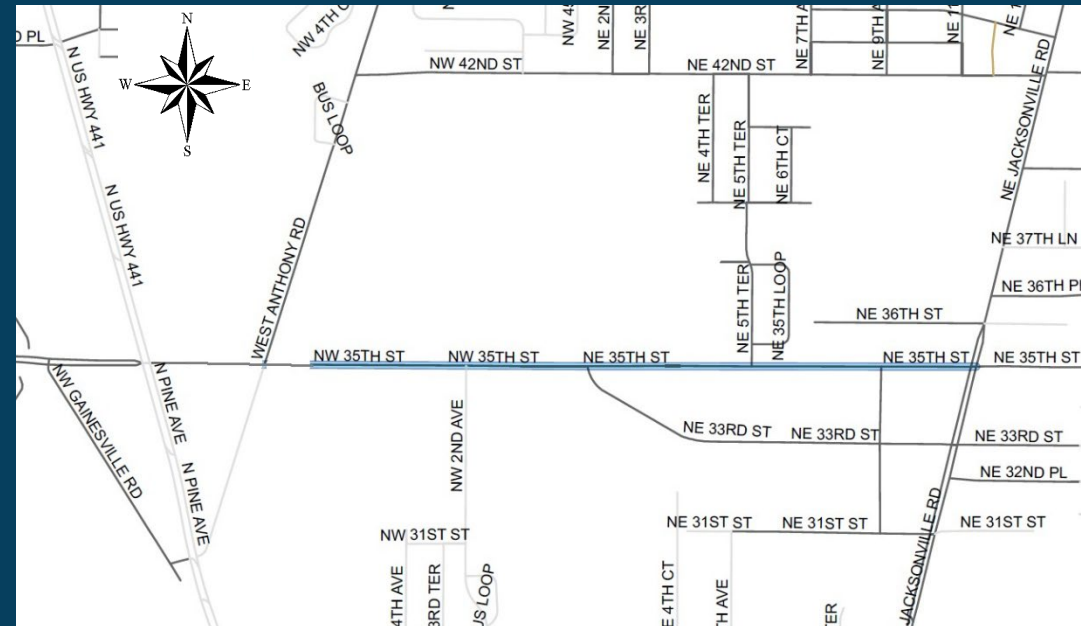

ADD LANES & RECONSTRUCT SIGNAL

- Pre-construction meeting scheduled for December 16, 2025.
- Notice to Proceed (NTP) estimated early January 2026.
- Finalizing acquisition of last parcel for DRA.

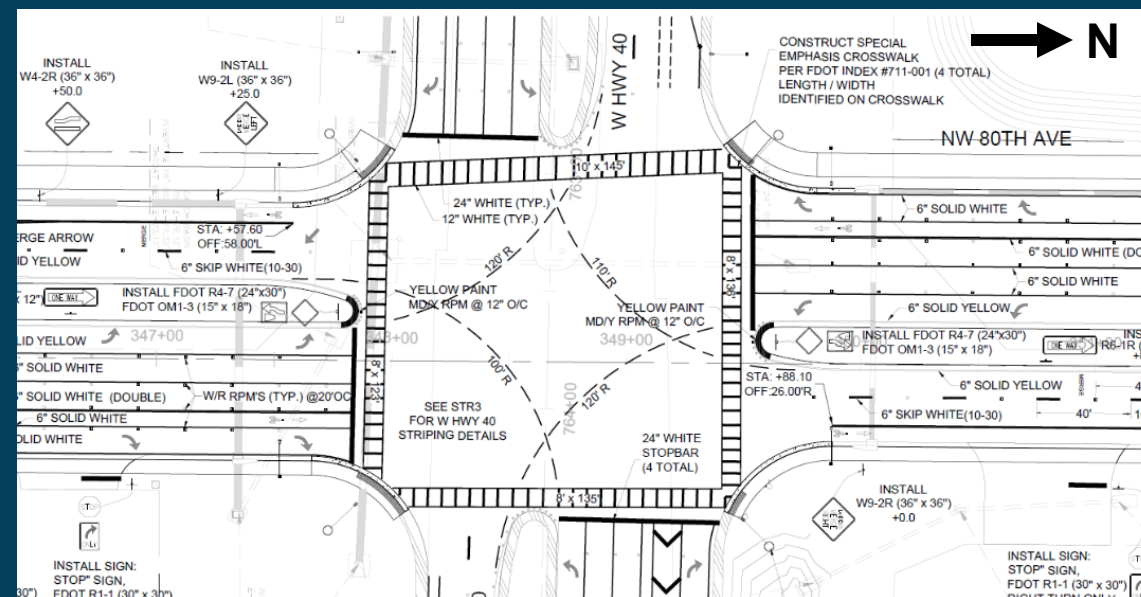

SW 38TH/40TH ST

ADD 2 LANES FROM SW 80TH AVE TO SW 43RD CT

- 60% design plans complete. Expect completion of 90% plans in January 2026.
- Coordinating with City of Ocala and FAA on right-of-way acquisition near airport.
- Coordinating with OTOW on cost-sharing for joint DRA proposed with Equine Center project.
- Anticipated Construction Advertisement between April and June of 2026.

