



ROADWAY PROJECT UPDATES FEBRUARY 2026 OFFICE OF THE COUNTY ENGINEER

1



SW 49TH/40TH AVE PHASE 1

NEW 4-LANE ROAD FROM SW 66TH ST TO SW 43RD ST RD

- SW 66th St Intersection Improvements
 - Phase 1 – Detour implemented Feb. 9th.
 - Phase 1 – Expected completion Apr. 10th.
- City approved design of left turn lane extension on SW 43rd St Rd.
- Design underway for turn lane improvements on SW 42nd St at SW 27th Ave.




2

SW 80TH AVE SEGMENT 1

ADD 2 LANES FROM SW 90TH ST TO 0.62 MILE N OF SW 38TH ST

- Agreements needed for road project heard today; OTOW, Pulte, Indigo East CDD, Bay Laurel Center CDD & Circle Square Ranch Master Association.
- Pre-construction meeting scheduled for Feb. 16th.
- Coordinating interlocal agreement with School Board.
 - Jan. 20th – Meeting with Principal & staff at West Port High School
 - Feb. 19th – Work Session with School Board
 - Feb. 24th – School Board Meeting

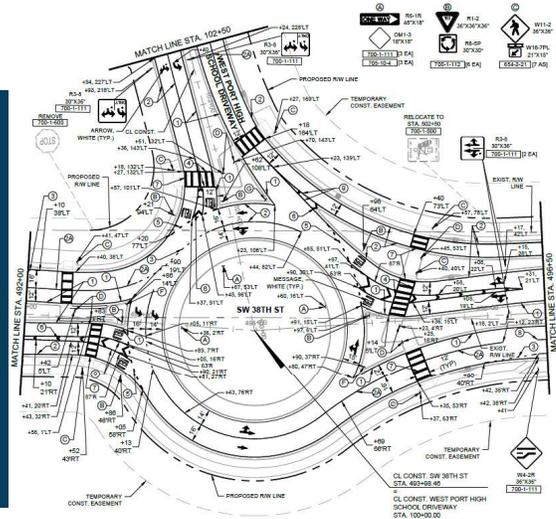

NW 80TH/70TH AVE SEGMENT 3

ADD 2 LANES FROM W HWY 40 TO N US HWY 27

- Actively negotiating right-of-way acquisition on 40 properties.
- Requesting right of entry agreement from World Equestrian Center (WEC).
- Construction advertisement estimated April 2026.
- Notice to Proceed (NTP) estimated June/July 2026.

