





ROADWAY PROJECT UPDATES
JUNE 2026
OFFICE OF THE COUNTY ENGINEER

SW 49TH/40TH AVE PHASE 1

NEW 4-LANE ROAD FROM SW 66TH ST
TO SW 43RD ST RD

- Remaining work at SW 66th St intersection (to be completed by June 19th).
 - Turn lanes on eastbound and westbound approaches.
 - Utility relocations.
 - Signal power, burn-in, & turn-on.
- FDOT closing SW 66th St bridge on June 15th.
 - Detour on next slide.



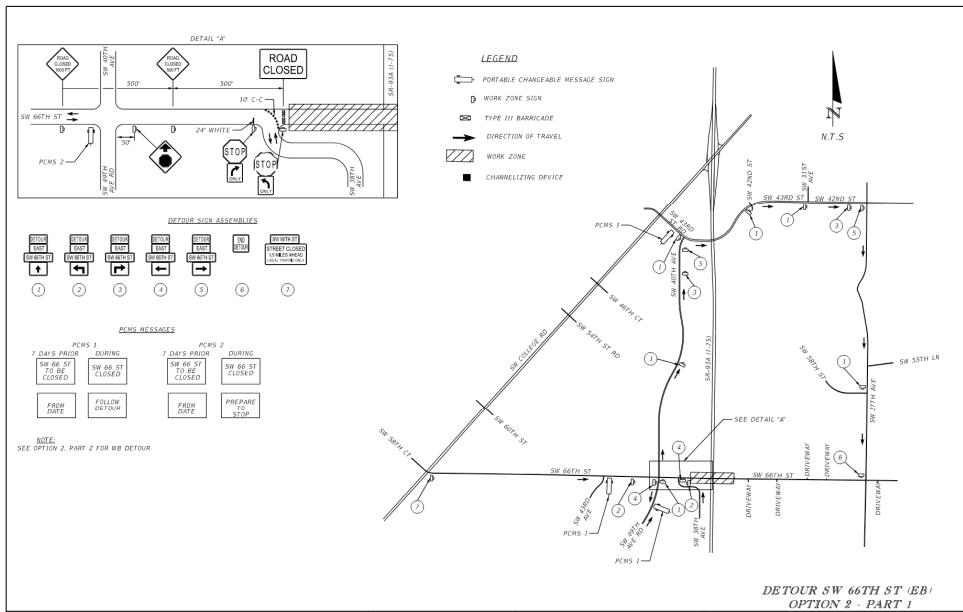

NW 80TH/70TH AVE SEGMENT 3


ADD 2 LANES FROM W HWY 40 TO N US HWY 27

- Bid opening scheduled for June 18th.
- Notice to Proceed (NTP) estimated mid-August.
- Right-of-way acquisition nearing completion.
 - 36 acquired or under contract.
 - 17 constructive negotiations.
 - 13 eminent domain.
- Finalizing utility coordination.



EMERALD RD EXTENSION

NEW 2 LANES FROM SE 92ND LOOP TO FLORIDA NORTHERN RR

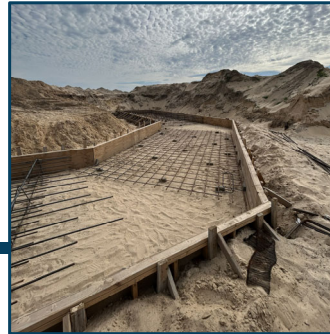

- Notice to Proceed (NTP): March 18, 2026
- Estimated Construction Completion: June 5, 2027
- Tunnel for cattle crossing under construction.
- Mass grading ongoing.
- Utility coordination with Duke Energy continuing.

