



ROADWAY PROJECT UPDATES JANUARY 2026 OFFICE OF THE COUNTY ENGINEER

1

RESURFACING PROJECTS



UNDER CONSTRUCTION

- E Hwy 316 – From NE 152nd Ct to NE 180th Ave Rd (2.9 miles)
- NW/NE 42nd St – From W Anthony Rd to NE Jacksonville Rd (1.2 miles)
- NE 7th Ave – From NE 42nd St to NE 49th St (0.5 mile)




2

SW 80TH AVE SEGMENT 1

ADD 2 LANES FROM SW 90TH ST TO 0.62 MILE N OF SW 38TH ST


- Finalizing agreements with OTOW, Pulte, Indigo East CDD, & Bay Laurel CDD.
- Interlocal agreement with Marion County School Board on January 27th school board meeting agenda.
- Notice to Proceed estimated February 2026.
- Right-of-way acquisition process continuing for Phase 1B.

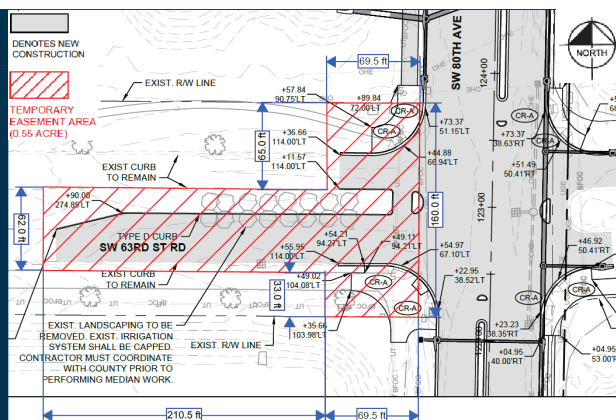

NW/NE 35TH ST PHASE 1B

ADD 2 LANES FROM 600 FT E OF W ANTHONY RD TO NE JACKSONVILLE RD


- Received permit from St. Johns River Water Management District on January 12th.
- Design completion estimated in June 2026.
- Updating appraisals for right-of-way on remaining 29 parcels.

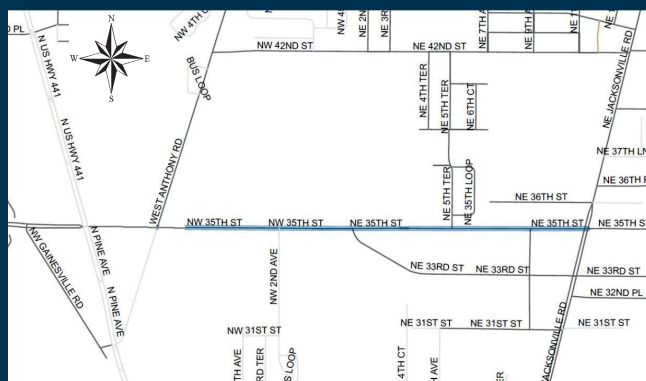

SW 49TH/40TH AVE AT SW 66TH ST DETOUR

5

Phase 1 – Detour Traffic to SW 38th Ave

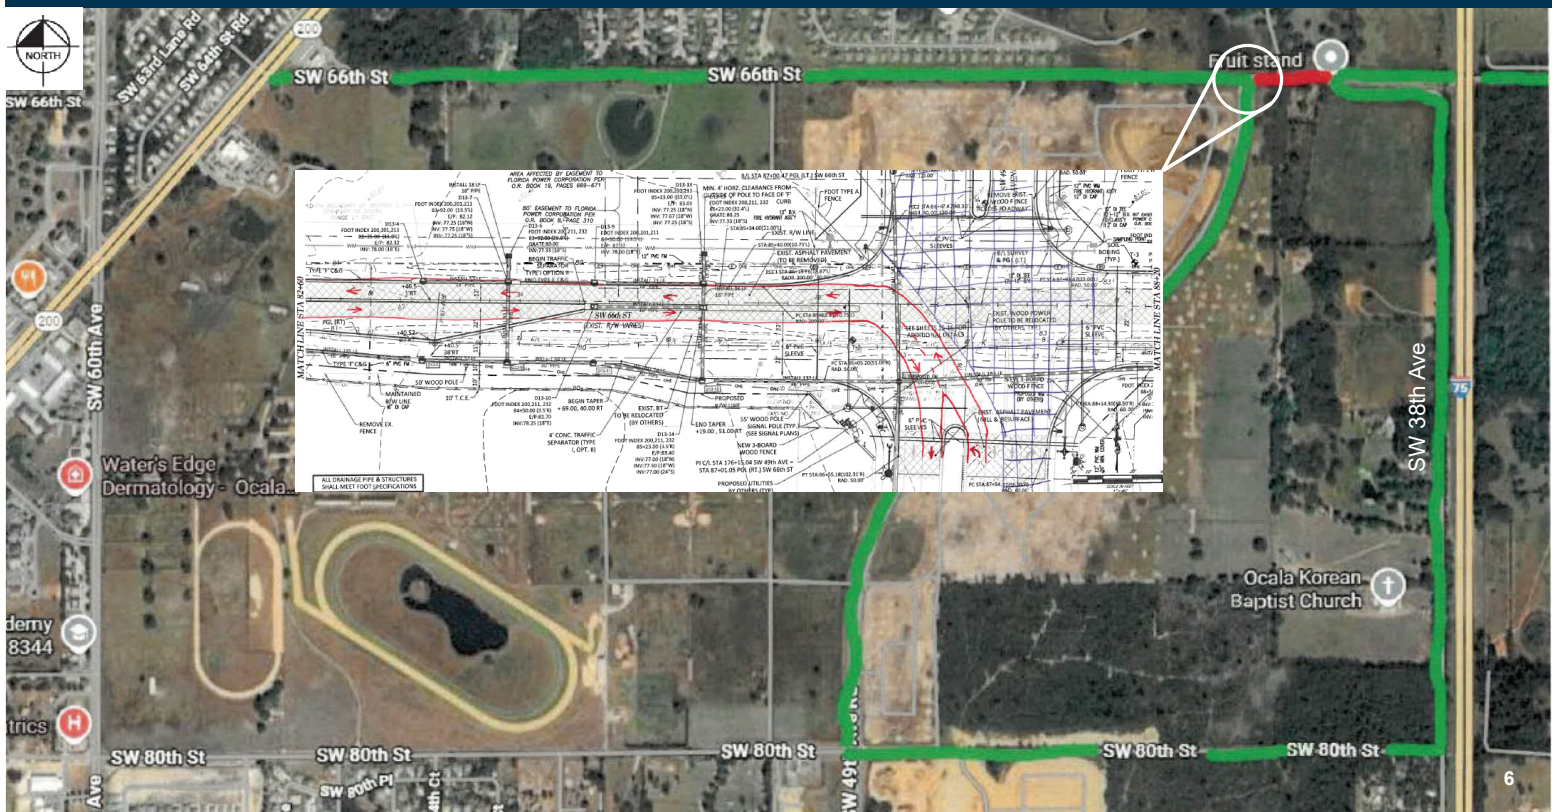

6

Phase 2 – Open 2 Lanes of SW 49th/40th Ave & Close SW 66th St

